

2023 Water Main Replacement & Street Improvement Project



Issue Date: September 15, 2023

PROJECT DESCRIPTION: The Village of Wauconda 2023 Water Main Replacement & Street Improvement Project is nearing its completion. The project was split into two separate phases of construction, North and South. The Downtown portion of the South project is substantially complete with work on-going in Hubbard Woods and Kent Avenue areas. The Village and HMG Engineers, Inc. will continue to provide weekly updates as they become available to provide the residents of Wauconda the most up-to-date information available. Please reach out to the respective personnel listed below with any questions you may have.

HUBBARD WOODS

WHAT TO EXPECT:

Helena Ave: All water main work and water service connections are complete!

George Ave: All water services have been reconnected and water main work will be complete Friday 9/15 - Saturday 9/16.

Orton Ave: Newly found lead services are causing a slight schedule delay. The Village and contractor are working with the affected residents to perform immediate inspections and coordinate replacement. The final water main reconnections cannot occur until all lead services are removed.

PAVING UPDATE: The contractor plans to start milling the existing asphalt the week of September 25 and install the first layer of asphalt that same week. There will be a week of utility adjustments before the final surface layer of asphalt will be installed. Weather and lead water service pending, the contractor is planning on substantially completing the project the 3rd week of October.



Hubbard Woods Anticipated Construction

Schedule (Week Starting)

9/11	9/18	9/25	10/2	10/9	10/16
Water Main & Water Services	Utility Adjust, Landscaping & Water Services	Milling, Asphalt & Water Services	Utility Adjust & Water Services	Final Asphalt Installation & Water Services	Pavement Striping & Final Landscaping

Future updates found at: www.wauconda-il.gov/ConstructionUpdates



Questions: HMG Engineers, Inc.
Scott Reisinger
(847) 668-3141

Village of Wauconda
Joe Coulter (Streets)
(847) 526-9610

Village of Wauconda
Bart Romero (Water)
(847) 526-9610

2023 Water Main Replacement & Street Improvement Project




KENT AVENUE

WHAT TO EXPECT (KENT AVE):

All water main installation and testing are complete. Thank you for your patience during the water service interruption to reconfigure the piping. New water service boxes were installed and one house connection was made. The remaining lead service houses are scheduled for replacement the week of September 25. The existing water main abandonment will occur following the reconnection of all water services.

PAVING UPDATE: The contractor plans to start milling the existing asphalt the week of September 25 and install the first layer of asphalt that same week. There will be a week of utility adjustments before the final surface layer of asphalt will be installed. Weather and lead water service pending, the contractor is planning on substantially completing the project the 3rd week of October.


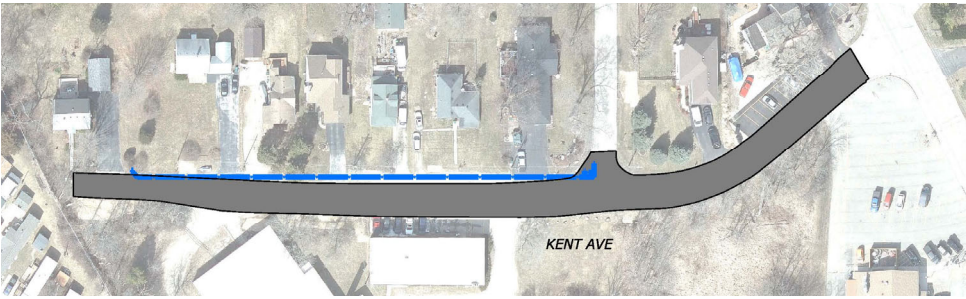


Kent Avenue Anticipated Construction Schedule (Week Starting)					
9/11	9/18	9/25	10/2	10/9	10/16
Minimal Activity	Minimal Activity	Milling, Asphalt & Water Services	Utility Adjustments	Final Asphalt Installation	Pavement Striping & Final Landscaping

DOWNTOWN

WHAT TO EXPECT (DOWNTOWN):

All work is complete except striping (anticipated week of 10/16). **Thank you for your patience in completing this important project!**

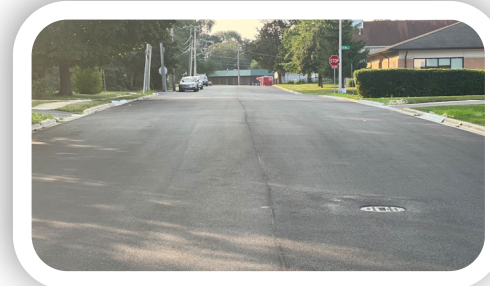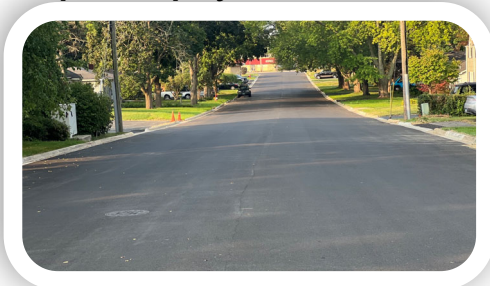

Future updates found at: www.wauconda-il.gov/ConstructionUpdates



Questions: HMG Engineers, Inc.
Scott Reisinger
(847) 668-3141

Village of Wauconda
Joe Coulter (Streets)
(847) 526-9610

Village of Wauconda
Bart Romero (Water)
(847) 526-9610
