

# 2023 Water Main Replacement & Street Improvement Project



Issue Date: August 29, 2023

**PROJECT DESCRIPTION:** The Village of Wauconda 2023 Water Main Replacement & Street Improvement Project is well underway. The project is split into two separate phases of construction, North and South. The Downtown portion of the South project is substantially complete with work on-going in Hubbard Woods and Kent Avenue areas. The Village and HMG Engineers, Inc. will provide weekly updates as they become available to provide the residents of Wauconda the most up-to-date information available. Please reach out to the respective personnel listed below with any questions you may have.

## HUBBARD WOODS

### WHAT TO EXPECT:


Helena Ave: Water main installation and all testing is complete. The contractor will be making service connection this week.

George Ave: Final connections to the existing water main are completed with pressure testing passed. Final chlorination results are pending followed by water service reconnections later this week.

Orton Ave: Water main installation is complete and pressure testing is occurring this week. Chlorination will follow for final main approval. Service connections are expected next week.

All sanitary sewer repairs and storm sewer installations are complete. The road improvement portion of the project will begin shortly following the completion of service installation.

Both properties that were found to have a lead water service will be contacted by Kerrigan Plumbing to schedule their new water service connection.

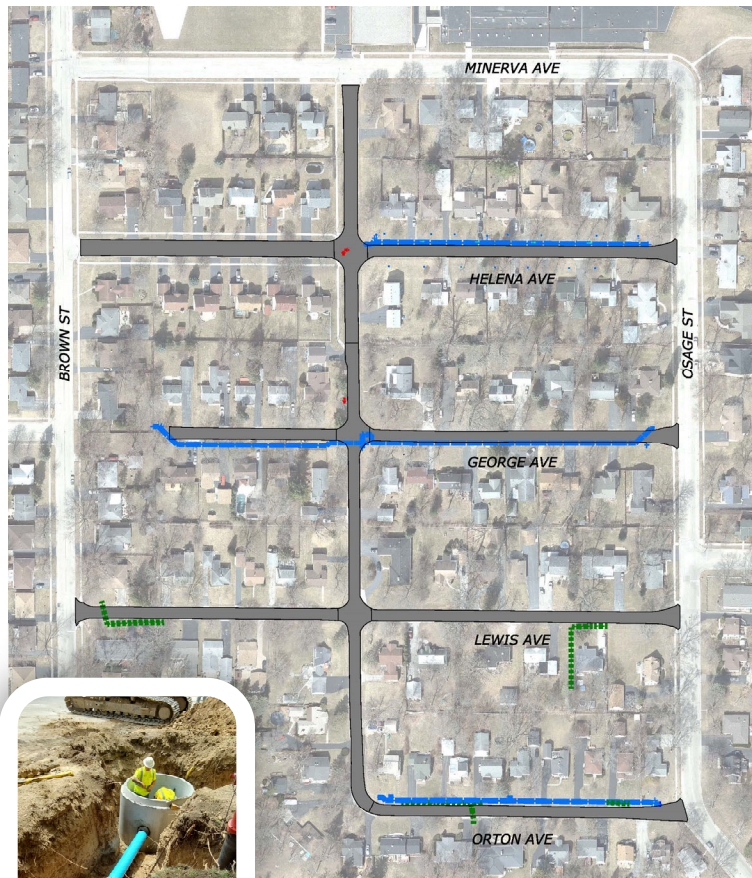

### Hubbard Woods Anticipated Construction

#### Schedule (Week Starting)

8/28	9/4	9/11	9/18	9/25	10/2
Water Main and Water Service Completion		Clean-up	Road Repairs Pending (more detail when available)		

Future updates found at: [www.wauconda-il.gov/ConstructionUpdates](http://www.wauconda-il.gov/ConstructionUpdates)



Questions: HMG Engineers, Inc.  
Scott Reisinger  
(847) 668-3141

Village of Wauconda  
Joe Coulter (Streets)  
(847) 526-9610

Village of Wauconda  
Bart Romero (Water)  
(847) 526-9610

# 2023 Water Main Replacement & Street Improvement Project




## KENT AVENUE

### WHAT TO EXPECT (KENT AVE):

All water main installation and testing are complete. Thank you for your patience during the water service interruption to reconfigure the piping. New water service boxes will be installed this week with one house connection being made. The remaining houses have lead service connections and require the plumbing to be completed in conjunction with the reconnection. Kerrigan Plumbing will be contacting the residents with lead services to schedule their improvements.

The contractor will next move to road repairs after the water main installation is complete. A more precise road improvement schedule will be provided closer to the completion of water main work.


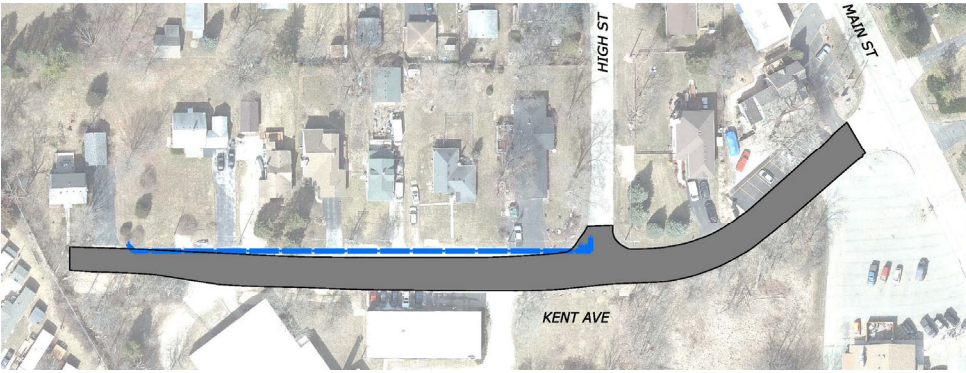


Kent Avenue Anticipated Construction Schedule (Week Starting)					
8/28	9/4	9/11	9/18	9/25	10/2
Water Main and Water Service Completion		Clean-up	Road Repairs Pending (more detail when available)		

## DOWNTOWN

### WHAT TO EXPECT (DOWNTOWN):

All work is complete except striping. **Thank you for your patience in completing this important project!**

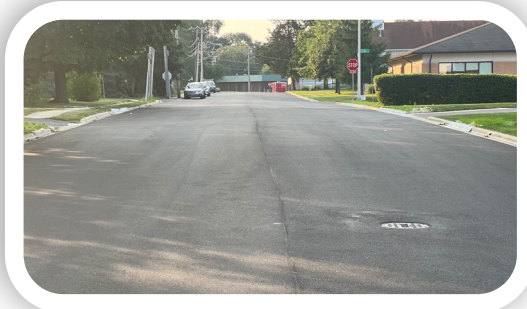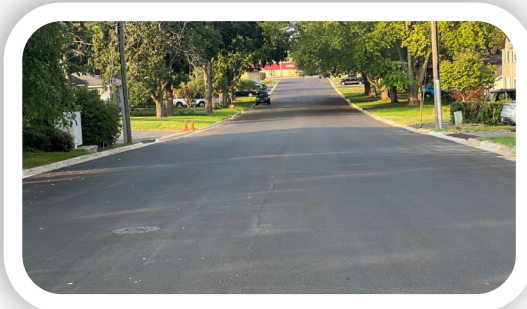

Future updates found at: [www.wauconda-il.gov/ConstructionUpdates](http://www.wauconda-il.gov/ConstructionUpdates)



Questions: HMG Engineers, Inc.  
Scott Reisinger  
(847) 668-3141

Village of Wauconda  
Joe Coulter (Streets)  
(847) 526-9610

Village of Wauconda  
Bart Romero (Water)  
(847) 526-9610
