Future updates found at: www.wauconda-il.gov/ConstructionUpdates


2023 Street Improvement Project



Issue Date: July 13, 2023

PROJECT DESCRIPTION: The Village of Wauconda 2023 Street Improvement Project (North) is underway with the construction having started on July 3rd. The project consists of storm sewer repairs, curb & sidewalk re-placement, asphalt milling and placement of varying depths of new asphalt. The project scope consists of Wauconda Road, Water Stone Subdivision, Apple Ridge Estates, Apple Country Subdivision, Karl Court & Dato Lane. See schedule below for updates as each phase of the project advances. The Village and HMG Engineers, Inc. will provide weekly updates as they become available to provide the residents and business owners of Wauconda the most up-to-date information.

RESIDENTIAL AREAS





Anticipated Construction Schedule (Week Starting)					
7/3	7/10	7/17	7/24	7/31	8/7
Concrete Curb / Sidewalk		Milling, Storm &	Storm Complete	Binder (1st)	Surface (2nd)
Storm Sewer & Start of Milling		Base Repairs	& Paving	Paving	Paving

WHAT TO EXPECT: Curb and sidewalk improvements are substantially complete in all areas. Punch list and final sidewalk work should be expected after all storm sewer work is complete in the Water Stone subdivision. Asphalt milling started July 13 and will proceed through next Wednesday (moving East to West). Base patching will round out the end of next week to address any subsurface failures in the road base.



Questions: HMG Engineers, Inc.
Phil Kochuparampil
(972) 838-5174

2023 Street Improvement Project



RESIDENTIAL AREAS






www.wauconda-il.gov/ConstructionUpdates Future updates found at:

Questions: HMG Engineers, Inc. Phil Kochuparampil (972) 838-5174

Future updates found at: www.wauconda-il.gov/ConstructionUpdates

2023 Street Improvement Project



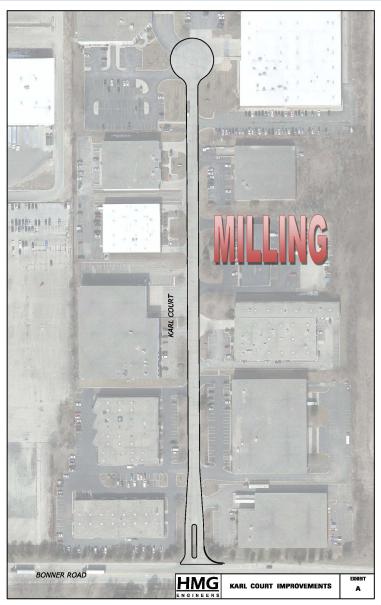

Dato Lane WHAT TO EXPECT:

The work involved on Dato Lane includes curb replacement, base patching, milling and asphalt installation.

All curb replacement is complete. Milling is expected to start next week with base patching planned for the end of next week.

Karl CourtWHAT TO EXPECT:

The work involved on Karl Court includes curb replacement, road widening of Karl Court at Bonner Road, base patching, milling and asphalt installation.

All curb replacement is complete. Milling is expected to start next week with base patching planned for the end of next week. A large base patch is pre-planned at the north end of the cul-desac to reinforce the road for truck turning purposes.

