


2023 Street Improvement Project



Issue Date: June 28, 2023

PROJECT DESCRIPTION: The Village of Wauconda 2023 Street Improvement Project (North) is getting underway with construction starting June 29th. The project consists of storm sewer repairs, curb & sidewalk replacement, asphalt milling and placement of varying depths of new asphalt. The project scope consists of Wauconda Road, Water Stone Subdivision, Apple Ridge Estates, Apple Country Subdivision, Karl Court & Dato Lane. See schedule below for updates as each phase of the project advances. The Village and HMG Engineers, Inc. will provide updates as they become available to provide the residents and business owners of Wauconda the most up-to-date information.

RESIDENTIAL AREAS

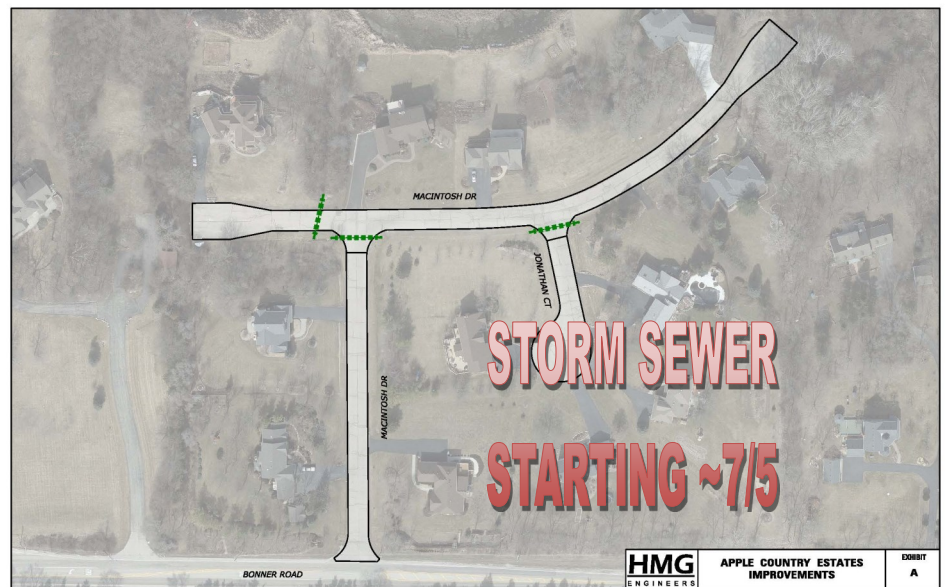

Anticipated Construction Schedule (Week Starting)

7/5	7/17	6/29	7/14	7/10	7/17	7/30
Storm Sewer		Concrete Curb & Sidewalk		Milling & Paving Prep	Paving & Restoration	

WHAT TO EXPECT: Curb and sidewalk saw cutting will start June 29th on Dato Lane, Karl Court, and the Water Stone and Apple Country Subdivisions. Curb, sidewalk, and storm sewer repairs (locations shown in green) are scheduled to start after the July 4th holiday. Milling and paving operations will commence once the storm sewer work and concrete work is complete. The schedule provided will be updated as the project progresses.

Future updates found at: www.wauconda-il.gov/ConstructionUpdates





Questions: HMG Engineers, Inc.
Phil Kochuparampil
(972) 838-5174

Village of Wauconda
Joe Coulter
(847) 526-9610

2023 Street Improvement Project



RESIDENTIAL AREAS

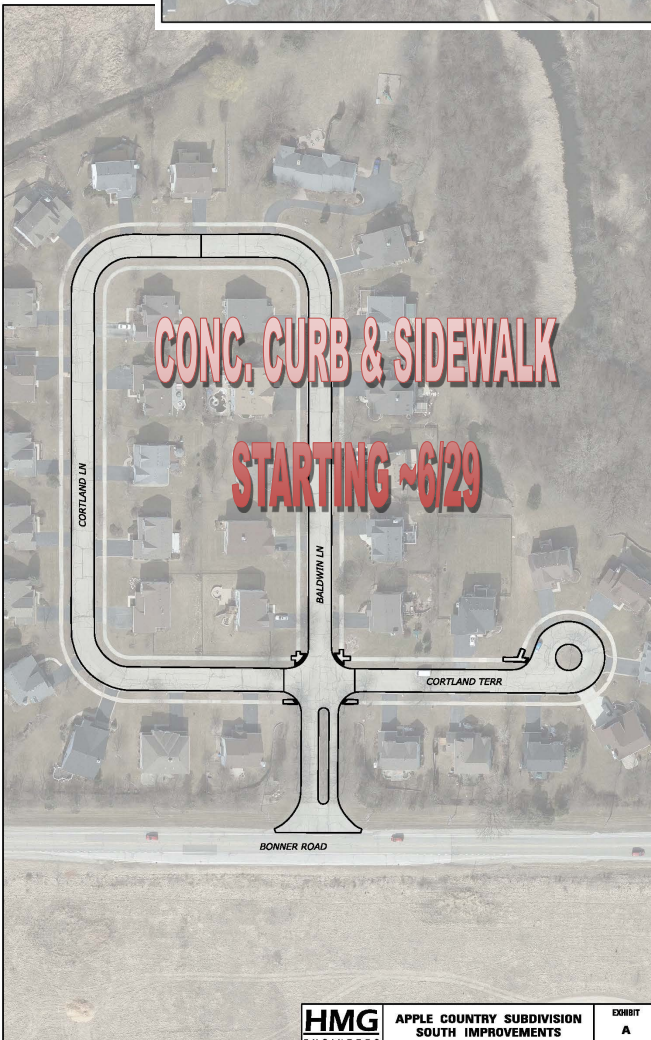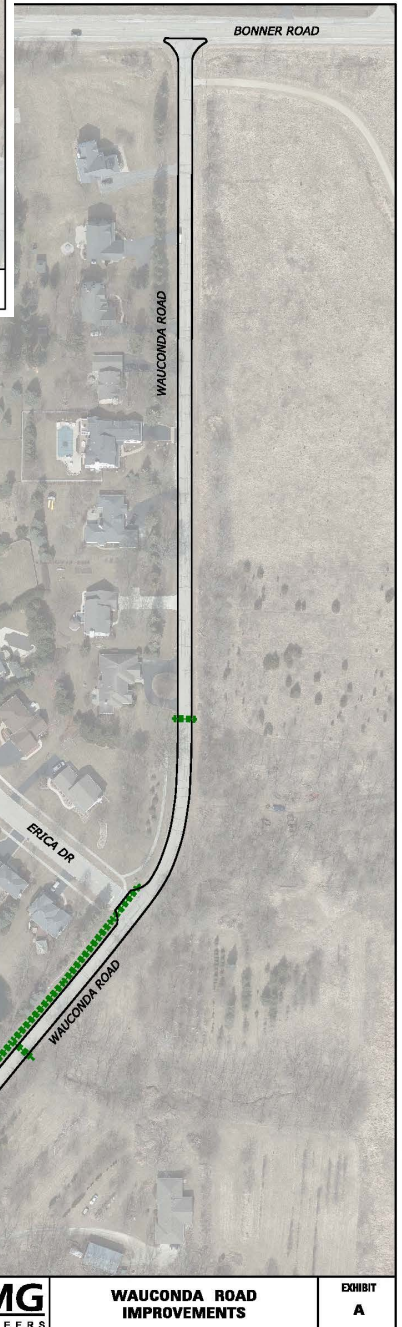

Future updates found at:
www.wauconda-il.gov/ConstructionUpdates



Questions: HMG Engineers, Inc.
Phil Kochuparampil
(972) 838-5174

Village of Wauconda
Joe Coulter
(847) 526-9610

2023 Street Improvement Project



Karl Court

WHAT TO EXPECT:

The work involved on Karl Court includes curb replacement, road widening of Karl Court at Bonner Road, base patching, milling and asphalt installation. There is a considerable amount of curb replacement necessary on Karl Court. The Resident/Business Project Representative from HMG Engineers, Inc. will be working with each business to find a feasible parking solution as we improve the corridor.



Dato Lane

WHAT TO EXPECT:

The work involved on Dato Lane includes curb replacement, base patching, milling and asphalt installation.

The Village and HMG Engineers, Inc. will provide a schedule with updates as they become available to provide the residents and business owners of Wauconda the most up-to-date information.

Future updates found at:
www.wauconda-il.gov/ConstructionUpdates



Questions: HMG Engineers, Inc.
Phil Kochuparampil
(972) 838-5174

Village of Wauconda
Joe Coulter
(847) 526-9610
