

2023 Street Improvement Project





Issue Date: August 3, 2023

PROJECT DESCRIPTION: The Village of Wauconda 2023 Street Improvement Project (North) is well under-way. The project consists of storm sewer repairs, curb & sidewalk replacement, asphalt milling and placement of varying depths of new asphalt. The project scope consists of Wauconda Road, Water Stone Subdivision, Apple Ridge Estates, Apple Country Subdivision, Karl Court & Dato Lane. See schedule below for updates as each phase of the project advances. The Village and HMG Engineers, Inc. will provide weekly updates as they become available to provide the residents and business owners of Wauconda the most up-to-date information.

RESIDENTIAL AREAS

PAVING SCHEDULED 8/7

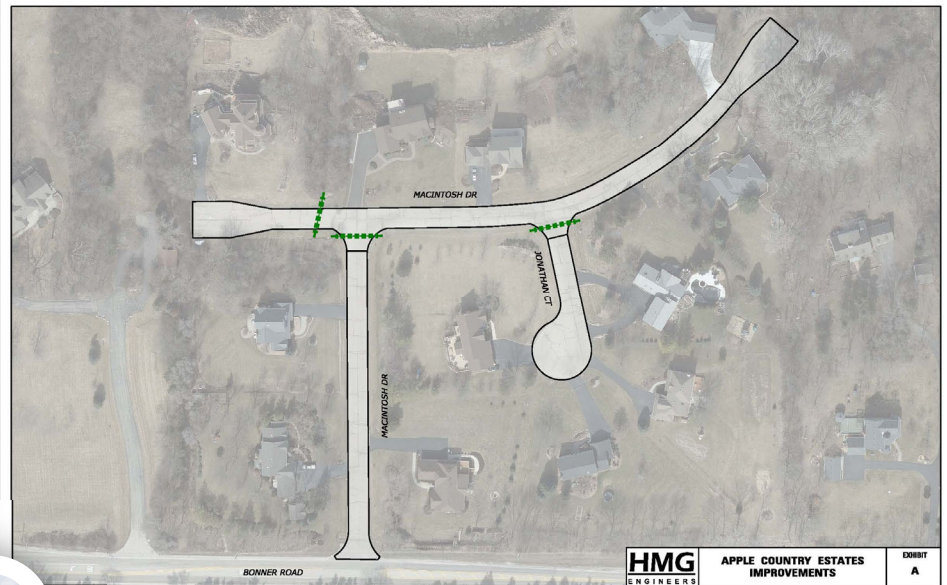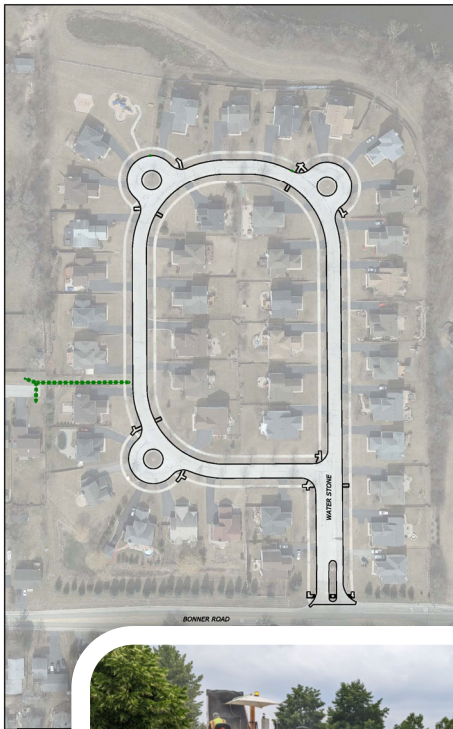

Anticipated Construction Schedule (Week Starting)		
8/7	8/14	8/21
Surface Paving	Shoulder & Landscaping	Shoulder & Landscaping

WHAT TO EXPECT: All storm improvements, curb work, base patching and binder asphalt have been completed. Peter Baker is targeting Monday August 7 to start the final surface layer of asphalt (starting location pending) with paving anticipated throughout the week. We thank you in advance for your patience as there may be small intervals where driveway access could be interrupted. Allowing the asphalt to cool down is necessary to having a great paving project. Thank you in advance for your patience.

Future updates found at: www.wauconda-il.gov/ConstructionUpdates




Questions: HMG Engineers, Inc.
Phil Kochuparampil
(224) 294-2047

Village of Wauconda
Joe Coulter
(847) 526-9610


2023 Street Improvement Project



RESIDENTIAL AREAS

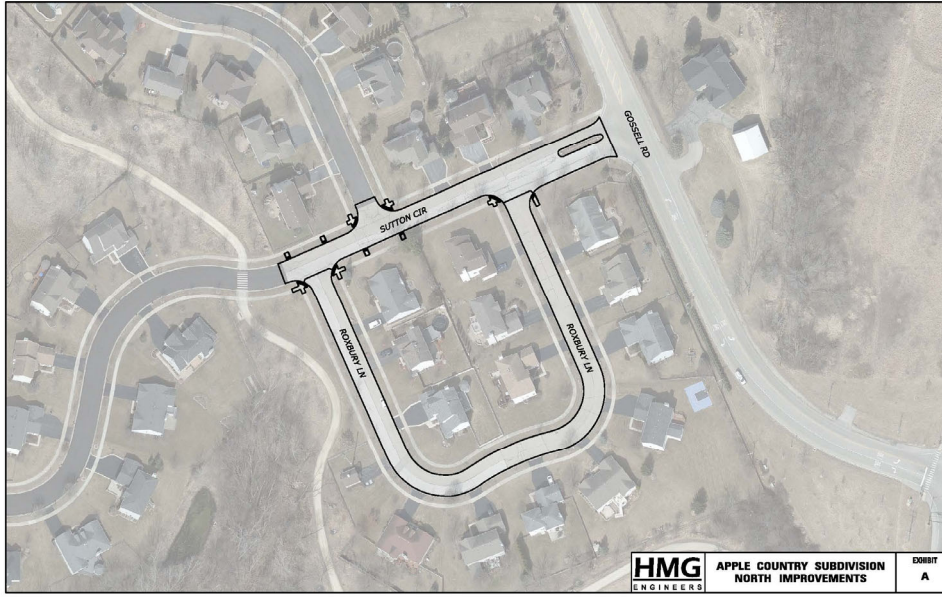


HMG ENGINEERS APPLE COUNTRY SUBDIVISION NORTH IMPROVEMENTS EXHIBIT A

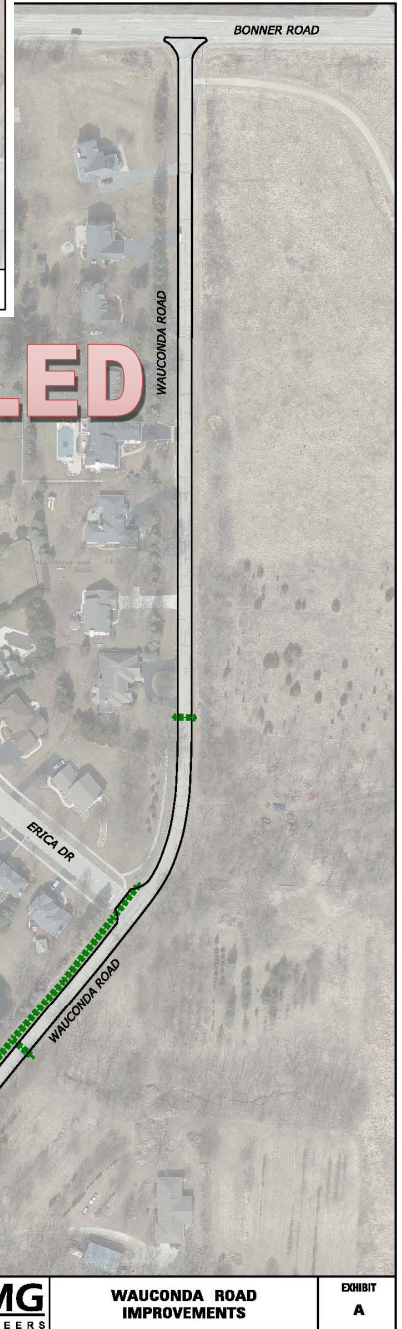

HMG ENGINEERS WAUCONDA ROAD IMPROVEMENTS EXHIBIT A

PAVING SCHEDULED TO START 8/7

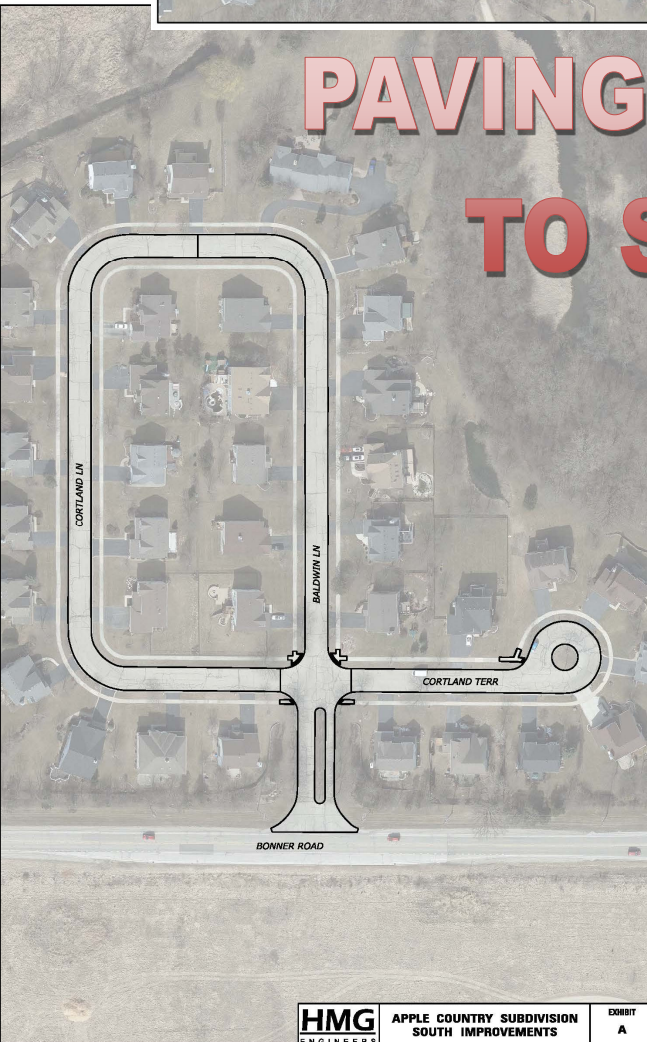

HMG ENGINEERS APPLE COUNTRY SUBDIVISION SOUTH IMPROVEMENTS EXHIBIT A

Future updates found at:
www.wauconda-il.gov/ConstructionUpdates



Questions: HMG Engineers, Inc.
Phil Kochuparampil
(224) 294-2047

Village of Wauconda
Joe Coulter
(847) 526-9610

2023 Street Improvement Project




Karl Court

WHAT TO EXPECT:

The work involved on Karl Court includes curb replacement, road widening of Karl Court at Bonner Road, base patching, milling and asphalt installation.

All curb, base patching, binder asphalt and landscaping work are complete. The only remaining items will be the installation of the surface asphalt (actual day pending) and ultimately pavement striping. We thank you for your patience in completing this important infrastructure project.

**PAVING SCHEDULED
TO START 8/7**

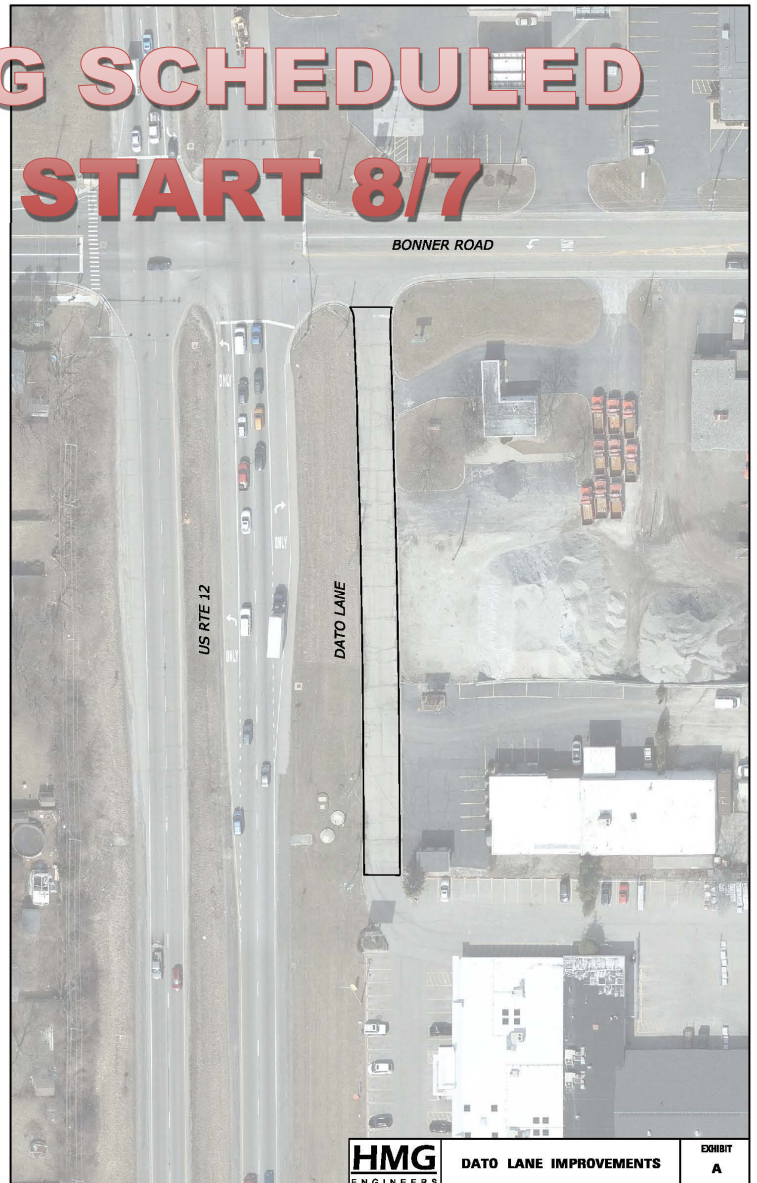

HMG ENGINEERS DATO LANE IMPROVEMENTS EXHIBIT A



HMG ENGINEERS KARL COURT IMPROVEMENTS EXHIBIT A

Dato Lane

WHAT TO EXPECT:

The work involved on Dato Lane includes curb replacement, base patching, milling and asphalt installation.

THANK YOU

Future updates found at:
www.wauconda-il.gov/ConstructionUpdates



Questions: **HMG Engineers, Inc.**
Phil Kochuparampil
(224) 294-2047

Village of Wauconda
Joe Coulter
(847) 526-9610
